



Status Report
RAC Project
Adams Ranger Station
Ranger's House
November 9, 2005



Wood routed sign.

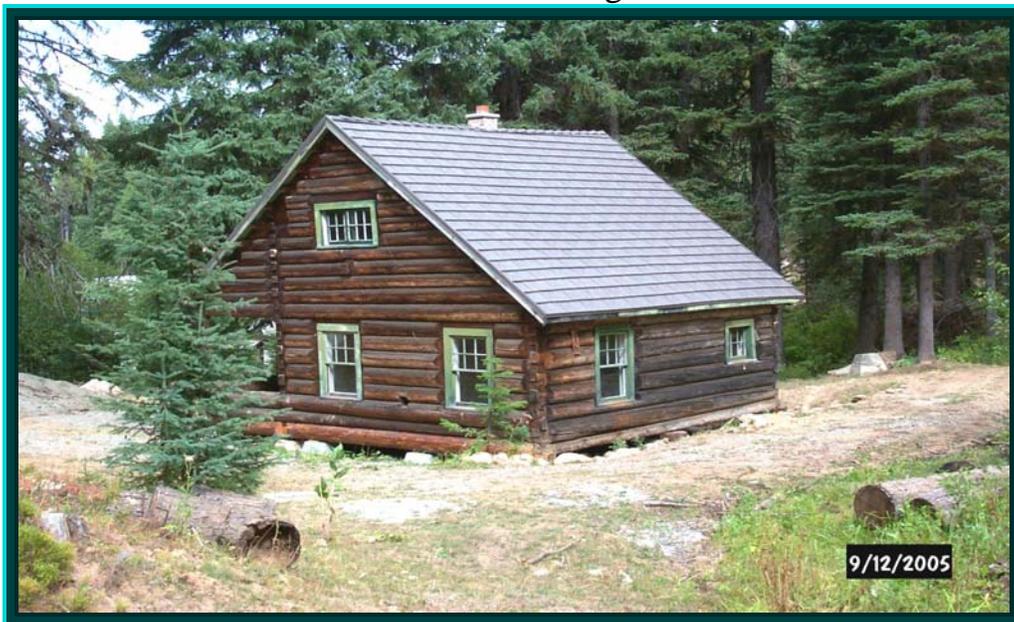

New aluminum shake roof on ranger's house.



The Salmon River Ranger District completed thinning around the Ranger Station compound to create a defensible space around structures.



Ceiling tiles and nails were removed.




New concrete block chimney in kitchen installed by local contractor Boyd Hopkins. Concrete block was used for the new chimney below the roof line.



Brick from the old chimney was used to build a new chimney above the roof line.



Bi-State Roofing Company removing old wood shakes and doing repairs to subroof.

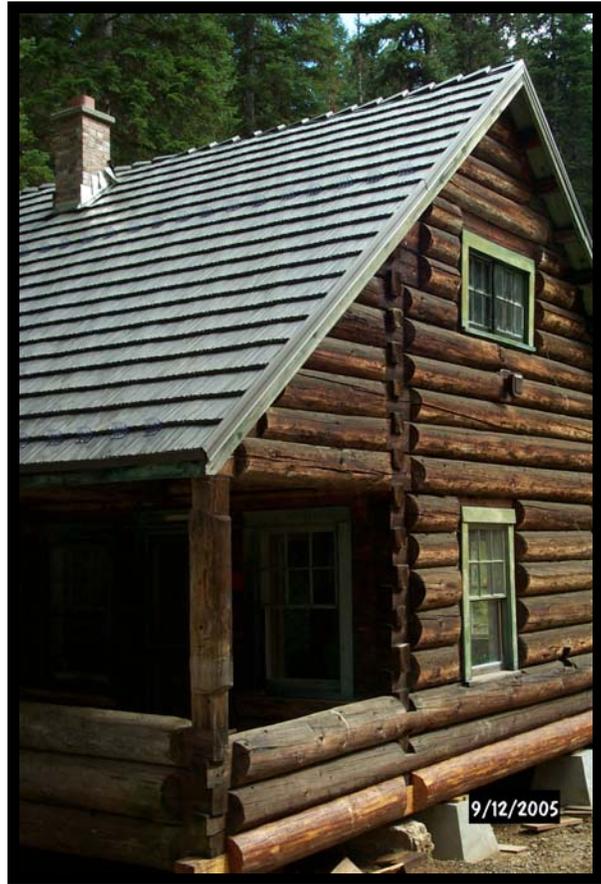

New aluminum shake roof on Ranger's House.
Funds Expended in FY 2005

Forest Service Employees	Labor	\$ 2,800.00
Boyd Hopkins	Construct new chimney	\$ 1,700.00
Bi-State Roofing	Install new aluminum shake roof	\$10,900.00
Grangeville Builders		
	Celetox (fiber board)	\$ 935.28
	Concrete pre-mix	\$ 67.80
	Chimney block	\$ 263.38
	Wood miner's wedges	\$ 45.43
Ace Hardware	Cleaning supplies, ant killer stakes, rat poison	\$ 39.33
Shroeder Log Home Supply	Oakum	\$ 215.90

Funds Expended in FY 2006

Condon Sign Shop	Routed/painted wood sign (Old Adams Ranger Station Established 1918)	\$ 323.28
Zumar Sign Co.	Adams metal road signs	\$ 120.00

Total \$17,410.40

With FY 2003-2006 expenditures there remains a balance of \$32,640.67 to complete restoration work.

In 2006 the restoration work will be completed. Work remaining includes: final leveling of building, refinishing of hardwood floors, installation and painting of celotex ceiling tiles and interior walls, replace interior trim, installation of cabinets and wood stove, refinishing and repairing of doors and windows, build back porch and stairs, install gray water tank, and install vault toilet.

Prepared by Cindy L. Schacher, Archaeological Technician
