

# Rapid River Trailhead

(03-002-17-2)

January 9, 2006




## Project Status:

- A Decision Notice and Finding of No Significant Impact to improve trailhead facilities on Forest Service lands adjacent to the Rapid River Fish Hatchery was issued in late-July 2005.
- Following public comment on the pre-decisional environmental assessment for the Rapid River Trailhead Facility, a modified alternative was developed that included phased improvements at both the “lower site” (as described in Alternative 2) and after a period of effectiveness monitoring consider development of the “hackberry flat” site (as described in Alternative 3).
- The Forest Service will begin the rights-of-way acquisition phase. Because of the number of ROW needed this phase could take up to two years to complete.
- Project implementation is tentatively scheduled in the Forest Capital Investment Program for FY2009. This will include only the “Lower Site”.


## Project Expenditures:

- |   |              |
|---|--------------|
| • Title II Funds approved ( for NEPA contract)            | \$ 33,750    |
| ○ Title II Funds spent                                    | 33,744       |
| • Forest Service Contributed Funds ( for NEPA completion) | <u>9,480</u> |
| • Total Project Cost to Date                              | \$ 43,224    |

# Rapid River Trailhead Alternative Map

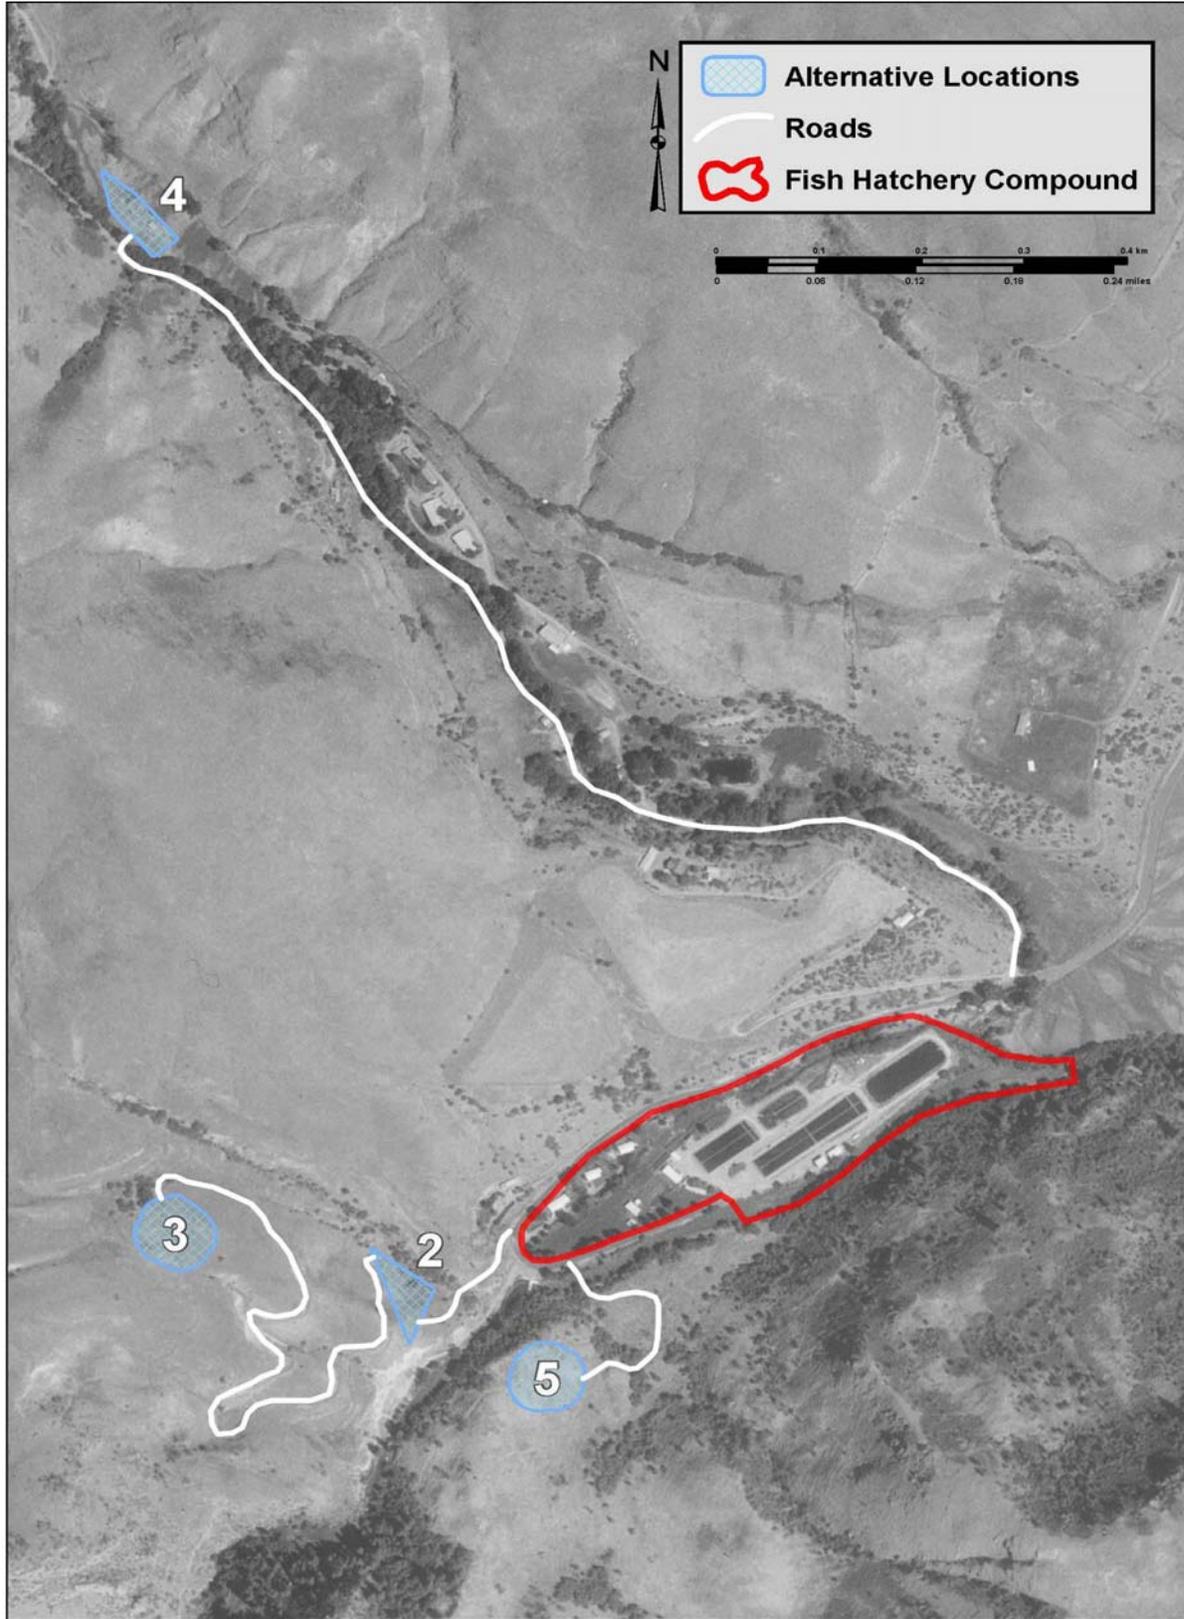

Rapid River Trailhead Conceptual Drawing – Phase 1 (Alternative 2)

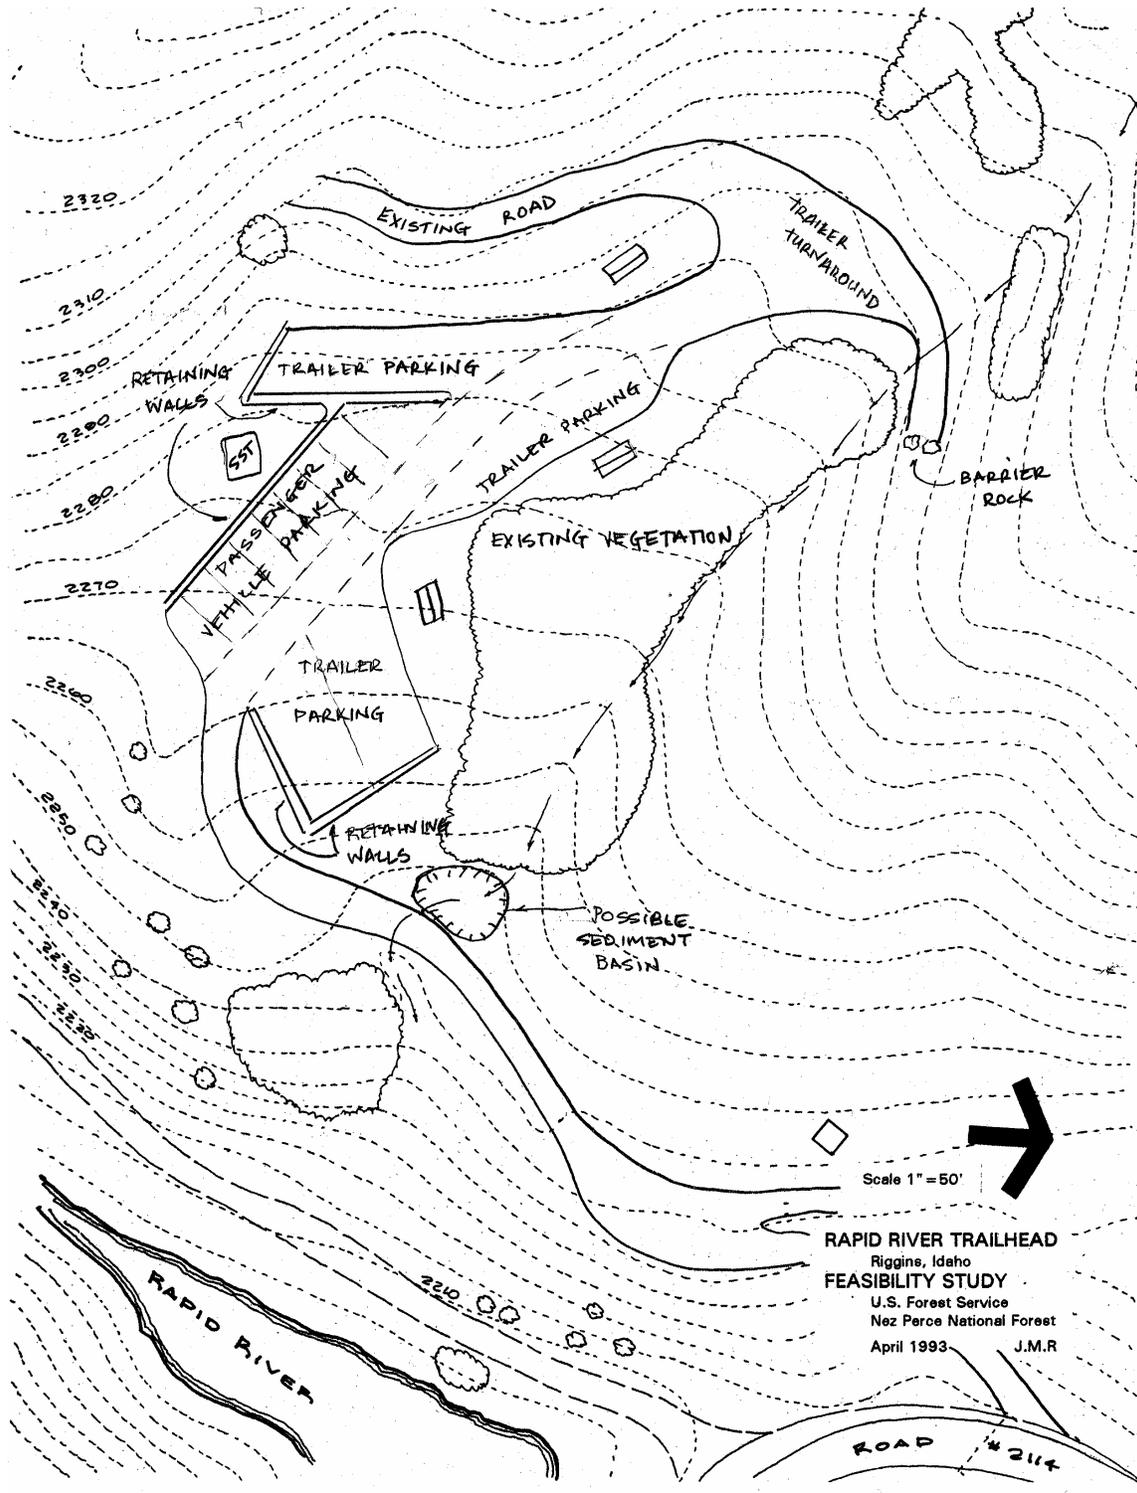

**RAPID RIVER TRAILHEAD**  
Riggins, Idaho  
**FEASIBILITY STUDY**  
U.S. Forest Service  
Nez Perce National Forest  
April 1993 J.M.R.
